

Project Freedom Industries	Report Number 6
	Date 12/14/2015
Task Interim Remedial Action	Project Number FRE-2015-364

Weather Conditions

Temperature Precipitation Predominant Wind Direction
 Min: 55 °F Max: 73 °F 0.25 in. Northeast

Did weather conditions cause delay in scheduled work Yes No
 Landfill approval also contributed to delay of scheduled work.

Safety


Safety Meeting Overview: Held daily safety meeting, reviewed SPSI Job Safety Analysis (JSA). SPSI participated in the safety meeting. All on-site personnel were instructed on PPE requirements and work zones. Additional hazards addressed (open excavations and distances to maintain from edges).

Attach sign in sheet from daily safety meeting and/or JSA review.

Air Monitoring:

	Yes	No	Details
MCHM/Benzene Tubes	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<u>Working in previously monitored areas.</u>
PPH Tubes	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<u>Working in previously monitored areas.</u>
PID	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>Completed by CORE.</u>
FID	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<u>Not available at this time.</u>

Location of ambient air monitors

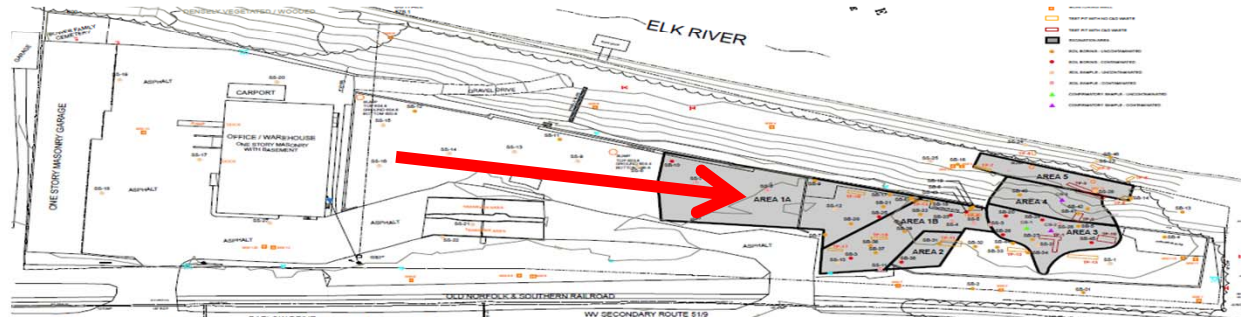

Draw predominant wind direction
 x = Downwind sample
 o = Upwind sample

Notes regarding air monitoring:

Air monitoring for MCHM and PPH was not performed on 12/14/2015.

Current Level of PPE in "Exclusion Zone" A B C D

Special Instructions/Details: The PPE listed in the SSHASP must be worn while working at the site. Access to the exclusion zone is limited to individuals in Level C PPE. Only necessary personnel are permitted in the exclusion zone.

Personnel

Contractors

Name	Job/Task	Company	Level of PPE	Respirator	
				Yes	No
Sotero Svingos	Excavation Oversight/Sampling	CORE	C	X	
Gary Houseman	Excavator Operator	SPSI	C	X	
Conner Fritz	Field Technician	SPSI	D		X
Ron Holmes	Excavator Operator	SPSI	C	X	
Michael Spencer	Field Technician	SPSI	D		X
Attach sheet for additional contractors, if necessary					

Erosion and Sediment Control

Previous 24-hour rainfall: 0.00 in.

Note: E&SC controls must be inspected following more than 0.5 inches of rain over a 24 hour period. All stormwater at the site must be collected and disposed of properly.

Erosion and Sediment Control Plan Sheet Number C 1 / C 2 / C 3

Are all erosion and sediment controls installed in accordance with the plan sheet listed above?

Yes No If no, provide details: _____

Is maintenance of the erosion and sediment controls required?

Yes No If yes, provide details: _____

Has the erosion and sediment control plan been revised?

Yes No If yes, redline the plan and provide details below:

Additional notes: N/A
